

kpc3+ inc settings:

cd software

bdelay 30 (300ms)




xmitlvl 411 3.1kHz dev @145Mhz

3.2kHz dev @ 430Mhz

configure db9 to take +V on pin 7

IC3210A TO KPC3+
WCS 31.9.1

EXCITER PCB (MAIN UNIT)

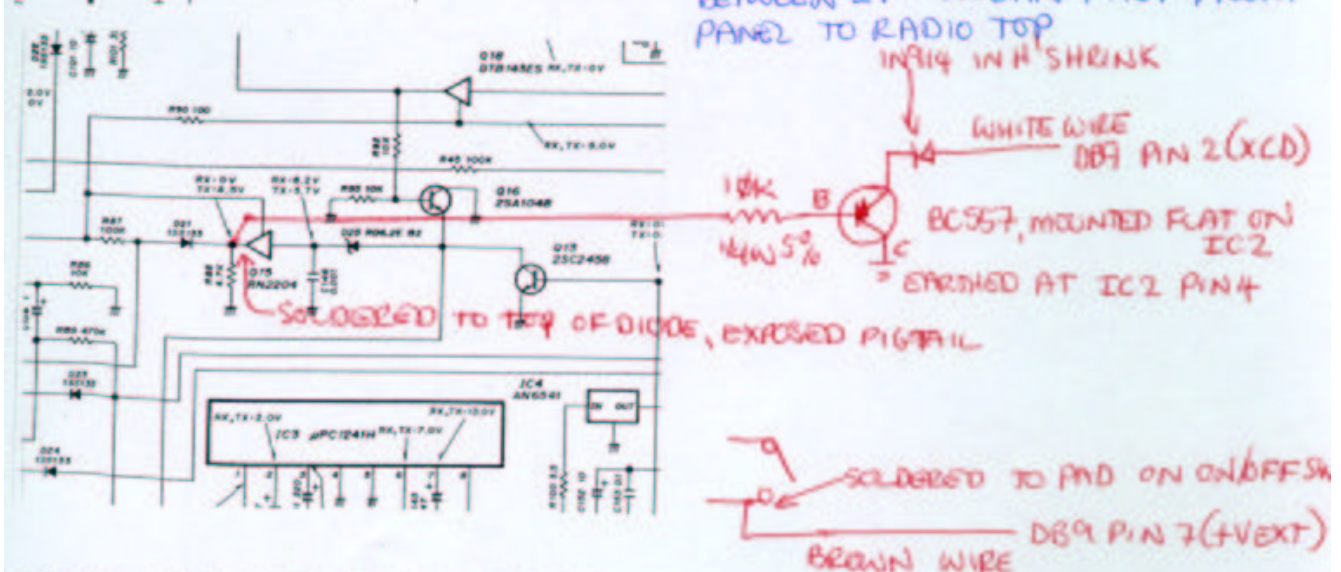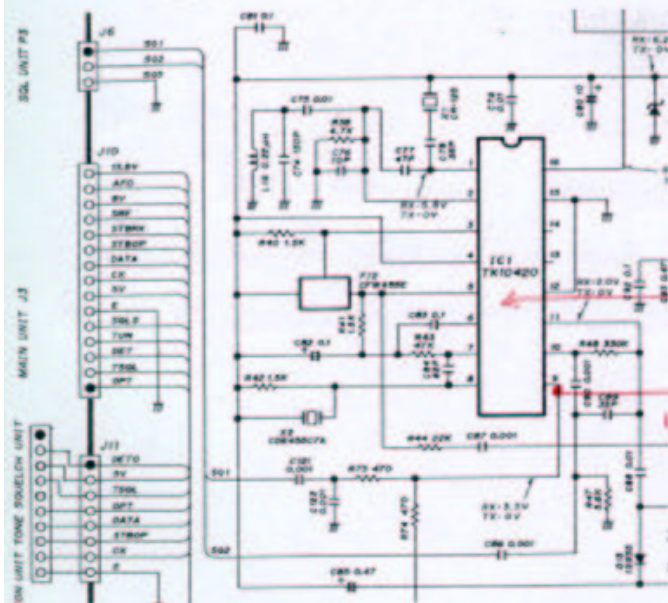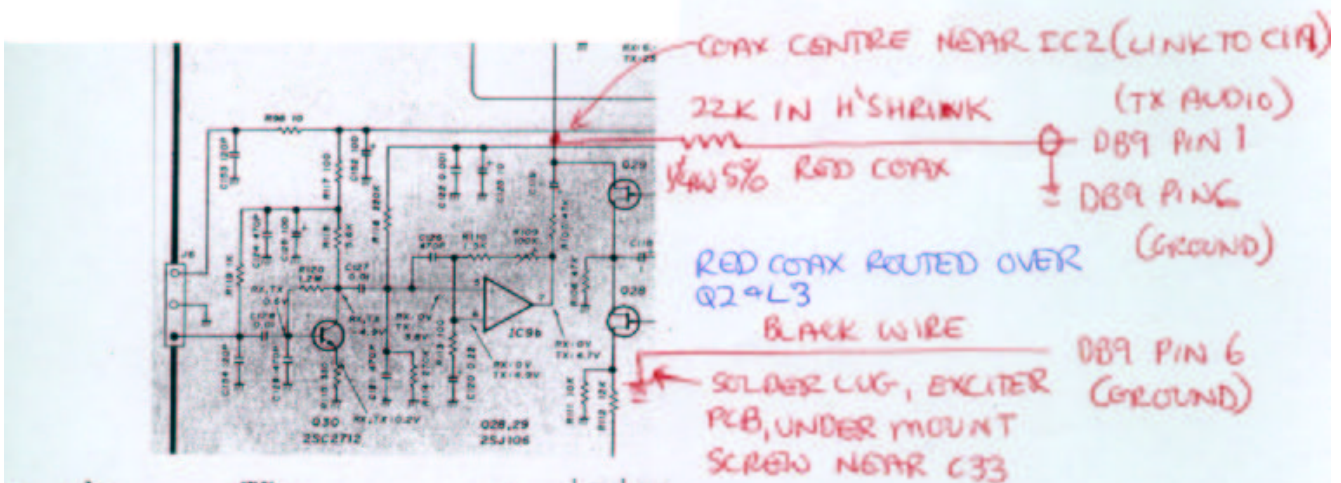

DB9m FOR KPC3+ CABLE ROUTED OUT HOLE WHERE EXT SPKR SOCKET HAS BEEN REMOVED (WIRING LINKED), RETAINED BY CABLE TIE.
